

Opportunity-to-Cash Workflow

Updated 31st July 2026

The Opportunity-to-Cash workflow is essential as it integrates Sales, Products and engineering, Operations, Procurement and Financial activities into a unified workflow, enabling consistent pricing (costing) accuracy, streamlined contract execution, timely and compliant invoicing, and dependable revenue recognition, thereby strengthening organizational efficiency, financial performance, and customer confidence.

C = CEO and MD

S = Sales

P = Procurement

O = Operations/PM

O = Owner

⊘ = Critical Control Point verified by Finance and Business Operations & Control

F = Finance

E = Product/Engineering

C = Contract Management/Legal

B = Business Operations & Control

1. Opportunity Qualification		2. Proposal Submission	
Customer Evaluation	S F	Scoping and defining the description of product/services (according to TOR/Customer Requests)	E S
Partner/Consortium/JV Evaluation (NDA is required)	S C F	Costing Effort estimation (resources & time plan)	O E S
Product and Solution Evaluation	E S	Pricing Modeling Defining conditions of proposed price Proposal Creation	S
Main Contractor Evaluation (especially one defined by customer)	P F	Risk Analysis with quantification	S E O P F
Oversea Supplier Evaluation (mandatory for new supplier)	P S F	COST SHEET Sign-off <Approval as in LOA>	S O ⊘
GO/NO GO Decision	CM F	GO/NO GO Decision	CM F


An O2C meeting shall be conducted during Step 1 or Step 2 whenever any of the following criteria is met:

- 1) Introduction of a new solution type.
- 2) Engagement with a new customer, or a customer with whom UTEL has had no business transactions for more than five years.
- 3) Expected project value of THB 50 million or above.
- 4) Estimated GP margin of 8% or below.

3. Commercial & Contracting	4. Project Handover & Kickoff	
Final pricing approval <Approval as in LOA> Customer Contract Legal & Commercial Terms & Conditions Payment terms and milestones, penalties (LD) Scope control clauses and change order Procedure defined in the contract	Meeting with Project Steering Group Handover from Sales/Presales to PM Project planning from PM - Objectives & Project Success Criteria - Key Stakeholders and Communication plan - Scope, Timeline (Milestones), Deliverables - Project Organization, Team & Roles (Interna/External Manpower, Subcontractor) - Project Financial Plan (budgets/costs and revenues)	In Step 3 or 4, if the Contribution Margin (CM) deviates from that established in Step 2 due to changes in revenue, costs, or both, the Project Manager (PM) and Sales shall revise the cost sheet and submit it for approval in accordance with the applicable LOA.
Partner/Consortium/JV Main Contractor Contract and Commercial Terms	Risk Registration Impact quantification Mitigation plan	The Project Kickoff Meeting shall be conducted jointly by the Sales and PM. Sales shall formally hand over the project to PM, and PM shall present the project delivery plan.
COST SHEET <u>Revised</u> Sign-off <Approval as in LOA>	COST SHEET <u>Revised</u> Sign-off <Approval as in LOA>	
GO/NO GO Decision		

5. Project Execution	6. Project Change Control	
Customer Engagement - Project Kickoff - Weekly or Monthly Project Progress Review Reporting/Meeting - Acceptance as per milestone in contract O S	Track Customer Change Request (CR) Revenue/Cost Impact CM/GP deviation S O	Cost Sheet Revision Process When Project Revenue or CM Changes A) The PM or Sales notifies BOC, or BOC identifies any changes and informs the PM and Sales (Trigger Point). B) BOC summarizes the reasons for the required Cost Sheet revision and submits them to F&A (within 1 business day). C) F&A provides the budget utilization information to the PM (within 5 business days). D) The PM and Sales revise the Cost Sheet and submit it to F&A for review (within 7 business days). E) After completing the review and finding no discrepancies, F&A proceeds with the approval process (within 7 business days). By working collaboratively and following this process, we can complete the Cost Sheet revision within 20 business days (or approximately a month). .To support this timeline: - From the initial stage, the PM should inform the Procurement team to request quotations only for high-value items, which are typically categorized under Materials and Subcontractors. - The PM and Sales team ensure that all information entered is accurate, complete, and properly documented to avoid rework,, or submission rejections.
Material and Project Inventory Management Inventory checking submission prior to new PO issuance O P <PR/ PO approval as in LOA>	Manage changes in Project Scope, Time, Resources, Costs O S P Track Internal Change Request (CR) Cost Impact CM/GP deviation	
Contractor/Subcontractor Management - PM provides capacity planning - Procurement evaluates and handles contracting - Managing non-performing P O <PR/ PO approval as in LOA>	Monitor and track Project performance Alert for CM/GP deviation Investigate for causes of deviation B O S	
Managing Customer Claim Penalty or LD O S C <Approval as in LOA>	COST SHEET <u>Revised</u> Sign-off O S <Approval as in LOA>	

7. Customer Invoice/Billing & Cash Collection Supplier Payment		8. Project Closure		In the event that insufficient budget is identified for any supplier payment before project closure, the cost sheet shall be revised accordingly.
Complete delivery log and acceptance document signed off by customer Trigger Customer Invoice based on milestones or project progress		Report project completion with final customer acceptance and payment	  	
Issue customer invoices Track customer payments Post cash receipts and reconcile accounts.		Financial reconciliation Confirm no outstanding AR or AP	   	
Manage escalation to customer to resolve delayed or aged receivables	 	Update in SAP • Status of CS orders • Pending subcon PO • Fund reserve	   	
Verify work completion Initiate subcontractor/supplier payments based on milestones Track payment status		Meeting with Project Steering Group • Project Summary, Objectives vs. Outcomes • Project Financial Performance • Key Achievements & Deliverables • Challenges & Resolutions • Lessons Learned • Next Steps (w/ Handover) & Formal Closure		
Manage supplier escalation To resolve delayed or aged payables	 			
COST SHEET <u>Revised</u> Sign-off <Approval as in LOA	  	Final Project Delivery Approval	 	

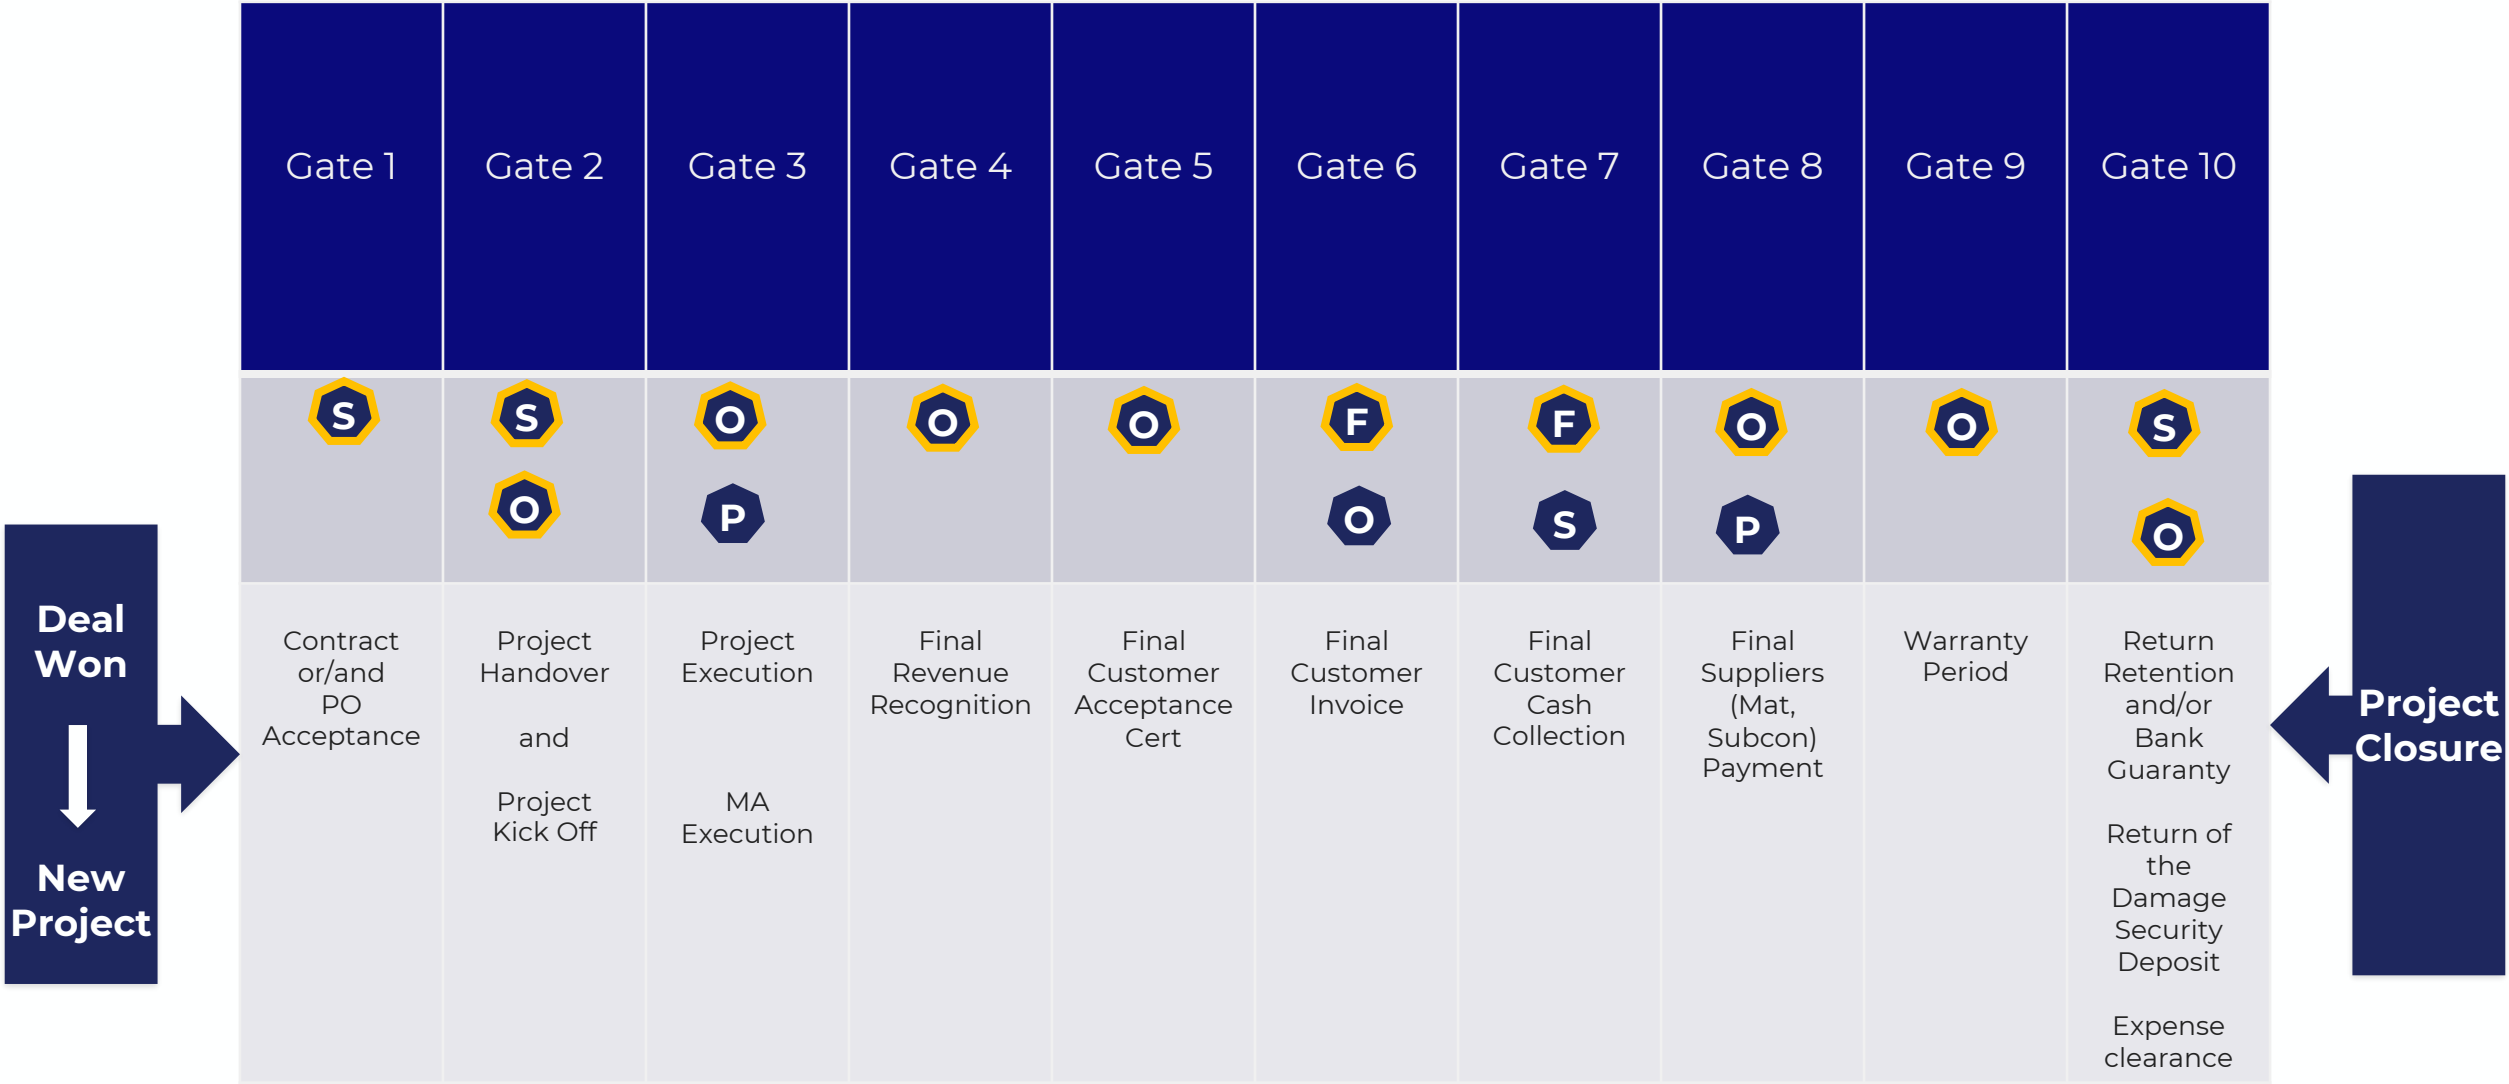



Thank You
